جامعة الحسين التقنية
Al Hussein Technical University

Professional Practice
40302211
L/618/7398

Section (0)

GROUP WORK

Assignment Title
We Do Training Events

Fall 2022 - 2023



Proposal for Training

Submitted To: Instructor Name

Submitted By:

Group Leader:

Students Names:

Table of Contents

PART 1 0

Executive Summary 0

Introduction 0

Objectives and Success Criteria 0

Target Audience 0

Guest Speakers 0

Planning Schedule 0

Event Schedule 0

Venue and Logistics 0

Basic Cost and Budget 0

Registration and Enrolment 0

Marketing and Promotion 0

Contingencies and Mitigation 0

Conclusion 0

Contact Information 0

References 0

Appendices * 0

PART II 0

Introduction 0

Problems Encountered 0

Problem Solving Application 0

Critical Reasoning Application 0

Methodologies 0

Event Evaluation 0

References 0

Introduction:

We are thrilled to present this proposal for our upcoming event that promises to be a revolutionary exploration of AI in the field of mobile applications. This event aims to bring together enthusiasts, experts, investors, and visionaries from the AI and mobile app development communities for an insightful and cooperative journey. As this event targets profitability through our sponsors, Ticket sales and partnerships.

Objectives and Success Criteria:

1.Profitability : (Timely, 2023)

Objective: making a good profit and covering all the expense paid throughout sponsors and varied type of registration fee of different tiers.

Success criteria : achieving a positive outcome by exceeding the revenue target and reaching the registering target also covering expense through the sponsorship Achieving higher attendees higher than the expected by posting on the social media before time and sending emails to the loyal participant that had the interest in technology also fixing up the thing that good bad reviews from the past events these stuff will lead to higher income from registration covering 100% of the revenue expense cost and covering having a profit

2.resource utilization:

Objective: monitoring our available resource and knowing to utilize our resource more effectively to ensure that it was productive as much as possible it prevent us to underuse our staff or (team member) or being overloaded by workload that were assigned to them.

Success criteria: splitting the multiple tasks to individual members based on the swot analysis and saw that each individual is taking the right time to complete each task and within time schedule and the plan also everyone was available one each task they had their utilization rate high above 70% which is calculated by time they have available which is the billable hour (the number of hours that the manager gives to the team member) multiply by the time taken from sponsorship .Moreover, increasing our profit form by giving other companies such as media companies by charging them for the advertisement placement fee such as putting next to the entrance and inside the venue.

3.Time allocation: (Grip, 2022) (Gravelle, n.d.)

Objective: Having a well-structured planning schedule and specification for the time for each task keeping it on budget makes the events flow run smoothly.

Success criteria: everything goes smoothly within the time located on each specific task and within the budget also making sure that everyone is delegate to working and grouping the small task trying to complete them all in one session putting them in a specific deadline. In addition, after measuring this stuff and creating a table to follow its also important to have a backup plan that if any of the time didn’t work there is backup plan

TARGET AUDIENCE

AI Experts and Researchers.

Developers and Programmers.

Technology Enthusiasts.

Investors.

Students.

General Public.

Guest Speakers:

Technical session provided by:

Special Guest Speaker - Dr. Shatha Emeeshat:

Profile:

Teacher at Bunat Alghad Acadmey

Education:

IT

SKILLS

TOOK A AI AND MOBILE APPLICATION COURSES

SESSION TOPIC:

1. **Future Trends in Ai**
2. **AI-driven Personalization in Mobile Apps.**

Special Guest Speaker - Dr. Jana Emeeshat:

Profile:

University Lecturer at Al Hussein Technical University (HTU)Education:

Education:

Case Western Reserve University .

Doctor of Philosophy - PhD, Electrical and Electronics Engineering Doctor of Philosophy - PhD, Electrical and Electronics Engineering .

Youngstown State University

Master's degree, Electrical engineering Master’s degree, Electrical engineering.

Skills:

- **Skills:** Python (Programming Language) · C (Programming Language) **Skills:** Python (Programming Language) · C (Programming Language)
- **Skills:** C (Programming Language)

Session Topic:

1.AI-powered Chatbots in Mobile Apps.

Workshops provided by:

HTU professor -Orwa Aladaileh

Profile:

Assistant Instructor - School of Computing and Informatics - Data Science and Artificial Intelligence Department

Education:

- **Master's Degree:** Computer Science, Al-Balqa' Applied University (BAU), 2003 - 2005
- **Bachelor's Degree:** Computer Science, Mutah University, 1999 - 2003
-

Experience

-Lead trainer \Team leader Lead trainer \Team leader. Orange Jordan.

-Senior Software Engineer \.Net Developer.
-System Engineer and Instructor.

Session Topic:

Phase 1 Introduction

1.Introduction to RunwayML with understanding the basics and Its Applications

2. setting up and installing of RunwayML of their Machines and set up a new project

3. Demonstrate how to navigate the user interface and the model market

Phase 2 Getting started

1.Setting up and installing of RunwayML of their Machines and set up a new project

2.demestion How to navigate user interface and access the market place

HTU professor -Lina Hammad

Profile:

Assistant Instructor - School of Computing and Informatics - Data Science and Artificial Intelligence Department

Education:

- **German Jordanian University - GJU:**
    - Master's degree, Computer Engineering
- **Al-Balqa Applied University:**
    - Bachelor’s Degree, Computer Software Engineering

Experience

- Al Hussein Technical University (HTU)

- Java Developer

-ADF Developer

Session Topic:

Phase 3: Model markets place

1.Generates tasks utilizing the market place

2. How to browse and preview select models based on project requirements

Phase 4 running the model

1.running the selected model based on the projects requirements and learn on how to send input requirement for each model

(Linkedin, n.d.)

Planning Schedule:

	Section 1	14						08/Nov	43d	60d	06/Jan				100%	
1	Define Event Objectives	HN, AH, KK						08/Nov	3d	3d	10/Nov			Finished	100%	HF A
2	Define Event Goals:	AH, HN, KK						11/Nov	1d	3d	13/Nov			Finished	100%	AF H
	Create Budget	Khair Khatatb...						14/Nov	13d	17d	30/Nov			Finished	100%	KK
4	Identify Potential Sponsors	Khair Khatatb...						14/Nov	4d	5d	18/Nov			Finished	100%	KK
5	Negotiation With Sponsors	Khair Khatatb...						19/Nov	5d	8d	26/Nov			Finished	100%	KK
6	Finalizing Deals With Sponsors	Khair Khatatb...						27/Nov	4d	4d	30/Nov			Finished	100%	KK
7	Select and Secure Venue	Adam Hasan						01/Dec	2d	4d	04/Dec			Finished	100%	AH
8	Identify and Confirm Key Speakers	AH, HN						05/Dec	4d	5d	09/Dec			Finished	100%	AF H
9	Develop Event Website	Adam Hasan						10/Dec	1d	2d	11/Dec			Finished	100%	AH
10	Develop Marketing Materials	Hala Nazzal						12/Dec	3d	3d	14/Dec			Finished	100%	HN
	Plan Workshop and Session Details	Hala Nazzal						15/Dec	6d	8d	22/Dec			Finished	100%	HN
12	Coordinate with Speakers	Adam Hasan						15/Dec	6d	8d	22/Dec			Finished	100%	AH
	Finalize Logistics	KK, HN						23/Dec	2d	4d	26/Dec			Finished	100%	KK H
14	Checking Event Necessities	AH, HN, KK						23/Dec	2d	4d	26/Dec			Finished	100%	AF H
15	Registration Setup	Adam Hasan						27/Dec	2d	2d	28/Dec			Finished	100%	AH
16	Attendee Communication	Hala Nazzal						29/Dec	2d	4d	01/Jan			Finished	100%	HN
17	Run-through and Rehearsals	AH, HN, KK						02/Jan	2d	2d	03/Jan			Finished	100%	AF H
18	Finalize Attendee Numbers	Khair Khatatb...						03/Jan	2d	2d	04/Jan			Finished	100%	KK
19	Address Last-Minute Details	Adam Hasan						05/Jan	1d	2d	06/Jan			Finished	100%	AH

Event Schedule:

Justifications for the time allocated:

First Day Activities:

9:00 - 9:30: Opening Ceremony

9:30 - 10:30: Technical session by Shatha AI in trends

10:30 - 12:30: Workshop by Dr. Orwa Phase 1 Introduction

12:30 - 01:00: Coffee break and snacks

01:00 - 02:00: Technical session by shatha AI-driven Personalization in Mobile Apps.

02:00 – 4:00: Workshop by Orwa. Phase 2 Getting started

04:00 – 05:00: Gala dinner

Second Day Activities:

9:00 - 9:30: Opening Ceremony

9:30 - 10:30: Technical session by jana AI-powered Chatbots in Mobile Apps.

10:30 - 12:30: Workshop by Dr. Lina Phase 3: Model markets place

12:30 - 01:00: Coffee break and snacks

01:00 – 3:00: Workshop by Phase 4 running the model

03:00-4:00: Awards ceremony and thanking people for attending the two-day events

04:00 – 05:00: Gala dinner

Venue and Logistics:

The Ritz-Carlton Hotel, represented by :

the Public Relations Manager: the link between us and the hotel management.

Reservations Officer: Appointments, pricing coordinator

Royal Hall: A hall that can accommodate 250 people,

consisting of a crew of 6 waiters, 2 greeters, and a technician when needed.

And a free parking for the attendees


Basic Cost and Budget:

Expenses				
Description	**Category**	**Quantity**	**Unit cost**	**Amount**
Hotel Hall	Location	2	5120	**10,240.00**
Room Rent	Location	2	225	**450.00**
Hall planning	Supplies	1	3,000.00	**3,000.00**
guest speaker	Program	3	50.00	**150.00**
notebooks	Other	150	1.00	**150.00**
mugs	Other	150	1.50	**225.00**
pen	Other	150	2.00	**300.00**
				-
			Total Expenses	**$ 14,515.00**

Income / Funding					
Description	**Unit Cost**	**Estimate Qty**	**Estimate Amt**	**Actual Qty**	**Actual Amount**
BLK coffee house			-		
Orange	1,000.00	1	1,000.00	1	
Arab bank	1,000.00	1	1,000.00	1	**1,000.00**
FiberTech	5,000.00	1	5,000.00	1	**5,000.00**
VIP tickets	150.00	30	4,500.00	30	**4,500.00**
Class A tickets	100.00	38	3,800.00	38	**3,800.00**
Single-regulrar tickets	50.00	74	3,700.00	74	**3,700.00**
invitation tickets	0.00	8	-	8	-
		Total	**$ 18,000.00**	**Total**	**$ 18,000.00**

Budget Summary	Summary of Expenses and Income
Total Expenses	**Expenses**

$14,565.00	Location	**$10,690**
Total Actual Income	Program	**$200**
$3,800.00	Food & Drink	**$0**
Balance	Supplies	**$3,000**
($10,765.00)	Other	**$675**
	Uncategorized	**$0**
	Total	**$14,565**



Registration and Enrolment:

Easy to buy ticket its outside the entrance

Having a varied in the ticket type Class A, Regular and VIP class

VIP class have different treatment they will have a special treatment such as a special parking place and extra 10-minute time to speak with the guest speaker

With different prices each making a profit and their table will be at the first row

For the A class they will have a better sight their table will be in the middle row

For the regular their table will be at the end.

Marketing and Promotion:

Brochures, Workshop Agenda, Website and an Instagram page

Contingencies and Mitigation:

Technical Issues: having backup equipment available, Have technical support on standby.

Speaker No-Show: fill the time with alternative content.

Health and Safety Concerns: Have first aid stations, medical personnel.

Contact Information:

Business Park, Amman

eliteeventssolutions2024@gmail.com

Tel: 123-456-7890

Fax: 123-456-7890

References

References

Gravelle, C., n.d. *The Importance of Time Management in Event Planning.* [Online]
Available at: https://eventeem.co.uk/the-importance-of-time-management-in-event-planning/
[Accessed 25 12 2023].

Grip, 2022. *7 tips for time management skills in events.* [Online]
Available at: https://www.linkedin.com/pulse/7-tips-time-management-skills-events-gripevents/
[Accessed 25 12 2023].

Jaime, 2022. *Event Planning: Defining Event Goals and Objectives.* [Online]
Available at: https://theeventscalendar.com/blog/event-management/defining-event-goals-and-objectives/
[Accessed 23 12 2023].

Oxford, U. o., n.d. *Setting event objectives |Communications Hub.* [Online]
Available at: https://communications.admin.ox.ac.uk/event-management-toolkit-setting-objectives#collapse1986591
[Accessed 23 12 2023].

Timely, 2023. *10 Strategies to Make Money from Events and Boost Revenue.* [Online]
Available at: https://time.ly/blog/strategies-to-make-money-from-events-and-boost-revenue/
[Accessed 25 12 2023].

*Appendices (Communication matrix, brochures, flyers, meeting log, emails, etc.).

STAKEHOLDER Identify the key stakeholders involved in the project or initiative. Please include the following information about each stakeholder: name, role.	External or Internal Stakeholder	COMMUNICATION OBJECTIVES Define the overall communication objectives for the project, including such goals as raising awareness, promoting engagement, providing updates, or gathering feedback.	RESPONSIBLE PARTY Indicate the person or team responsible for delivering each message. Doing this helps ensure accountability and clarity.	COMMUNICATION METHODS List the various communication channels that you will use to reach stakeholders. These channels can include email, newsletters, social media platforms, Face to Face, Screen to	FREQUENCY Determine the frequency and timing of communication activities. Such activities can include providing regular updates, highlighting events, or disseminating any other time-sensitive information (As Needed, Once, Daily, Weekly, Bi-Weekly, Monthly Bi-Monthly,	TIMING If Date or time required specify.	COMMENTS

				Screen, websites, meetings, workshops, or any other relevant medium.	**quarterly, yearly).**		
Beyond-Digital-Wave	External	Discuss the proposal and providing updates, seeking approval	Elite Events Solutions Team	Email and meetings	As Needed	Before 8th of November	Regular updates on the event planning (Budget, is everything smooth) and once the event finished, they should be update about the feedback of the attendees on the topic
HTU Professors	External	Outlining workshop details, goal and the expectation, and confirming collaboration.	Elite Events Solutions Team	Email	Once initially, then As Needed	5 of December	Regular updates on workshop schedules and the goals that we want to achieve
Sponsors	External	Discuses sponsorship collaboration, share the benefits and a meaningful collaboration	Elite Events Solutions Sponsorship Manager	Phone Calls, Meetings	Monthly leading up to the event	4 of November to 27 of November	Continuous updates on sponsorship packages, Benefits and the interest .
Elite Events Solutions	Intern	Discussing everything and the achieved goals in the event	Entire Sparks elite Team	Team Meetings, Internal	WEEKLY	Throughout Planning and during the event	Keeping them in progress about the event and the problem that we faced and how we solved it

	al			Emails			
Finance Team	Internal	Budget updates, financial coordination for sponsorships and the registration	Technical Coordinator	Internal Emails, Meetings	Bi-Monthly	Throughout Planning	Keep updating on the budget needed for the sponsorships, and planning for the event.
Marketing Specialist	Internal	Promote the event, share updates and guidelines for participants	Elite Marketing Specialist	Messages screen to screen And phone calls	Regularly	Throughout Planning	Engaging content, promotional posts, and important updates to promote the event and keep participants informed.
Venue Manager	External	Determine the hall details, and confirm cooperation	Elite Events Solutions Team	Emails and phone calls	Bi-Weekly	1 to 4th of December	Regular updates on event setup, logistics, and venue-specific requirements and the size that we want the theme that we wanted to be
Guest Speakers	External	Outlining Technical session details and confirm the goals and expectation, and confirming collaboration.	Elite Events Solutions Team (Adam)	Email, Meetings	Bi-weekly	Until 8 of Jan last day of the event	Regular updates on technical session details, goals, and expectations throughout the planning of the event
IT Support Team	Int	Ensure technical infrastructure	Elite Events	Email, phone	As Needed	Before and during the event	addressing technical issues promptly before and during the event and addressing that technical issues that we might face

	e r n a l	readiness, resolve IT-related issues	Soluti ons Techn ical Coord inator (khair)	calls, Face to face			

PART II



Meeting Confirmation for Hall Booking at The Ritz-Carlton

Inbox ×

tareq ayesh <RitzCarltonAmman@gmail.com>
to khairkhb

1:17 PM (6 minutes ago)

Dear Khair Alabdallah,

I hope this email finds you well. We appreciate your interest in hosting an event at The Ritz-Carlton. We are pleased to confirm our availability for a meeting to discuss and finalize the details of your hall booking.

Here are the proposed details for our meeting:

Date: 18 December 2023
Time: 2:30 pm
Location: The Ritz-Carlton Amman
Address: 5th circle Amman, Zahran St, Amman 11892

Best regards,

tareq ayesh
Communication manager
The Ritz-Carlton, Amman
(06) 550 0000

Reply Forward

New Message from Mail Delivery Subsystem. Show






Elite Events Solutions
BEYOND DIGITAL WAVE
TECHONOLOGY

Elite Events Solutions


Elite Events Solutions

spark.elite_

7 Posts

8,829 Followers

2,207 Following

Spark Elite

Elite Events Planner | Crafting Unforgettable Moments | Transforming Dreams into Reality ✨

Over 20 year of excellence 🥂

Amman, Jordan

eliteeventssolutio.wixsite.com/elite-e...

Edit profile

Share profile















Elite Events Solutions

2-DAY TRAINING



Get started
You'll be
Learning about
designing
mobile
application
using AI



Sunday 7, Jan - 8, Jan

9:00 AM - 5 :00 PM

Ritz Cartlon Hotel

SIGN UP NOW!

BEYOND DIGITAL WAVE
TECHONOLOGY

ABOUT OUR TRANING

We aims to provides the participant the knowledge on how to use AI in designing mobile application by holding technical sessions that are delivered by expert Jordanian speakers and workshops which is delivered by HTU Professors on both day of the events

CONTACT US

Business Park, Amman
Tel: 123-456-7890
https://eliteeventssolutio.wixsite.com/elite-events-solutio

TOPICS

that will be covered :

TECHNICAL SESSIONS

1.Introduction to AI in Mobile App Development.
2.AI-powered Chatbots in Mobile Apps.
3.AI-driven Personalization in Mobile Apps.

By :Dr. Jana Emeeshat

WORKSHOPS SESSION

1.Introduction to RunwayML with understanding the basics and Its Applications
2. setting up and installing of RunwayML of their Machines and set up a new project
3. Demonstrate how to navigate the user interface and the model market
1.Setting up and installing of RunwayML of their Machines and set up a new project
2.demestion How to navigate user interface and access the market place
1.Generates tasks utilizing the market place
2. How to browse and preview select models based on project requirements
1.running the selected model based on the projects requirements and learn on how to send input requirement for each model

By : Dr.lina hamad & Dr. Orwa Aladaileh from HTU Professors


REWARDS

by attending our training sessions you will be rewarded an certificate given
by Beyond digital wave company.

AI EVENT

Read-only view, generated on 01 Jan 2024

Instagantt

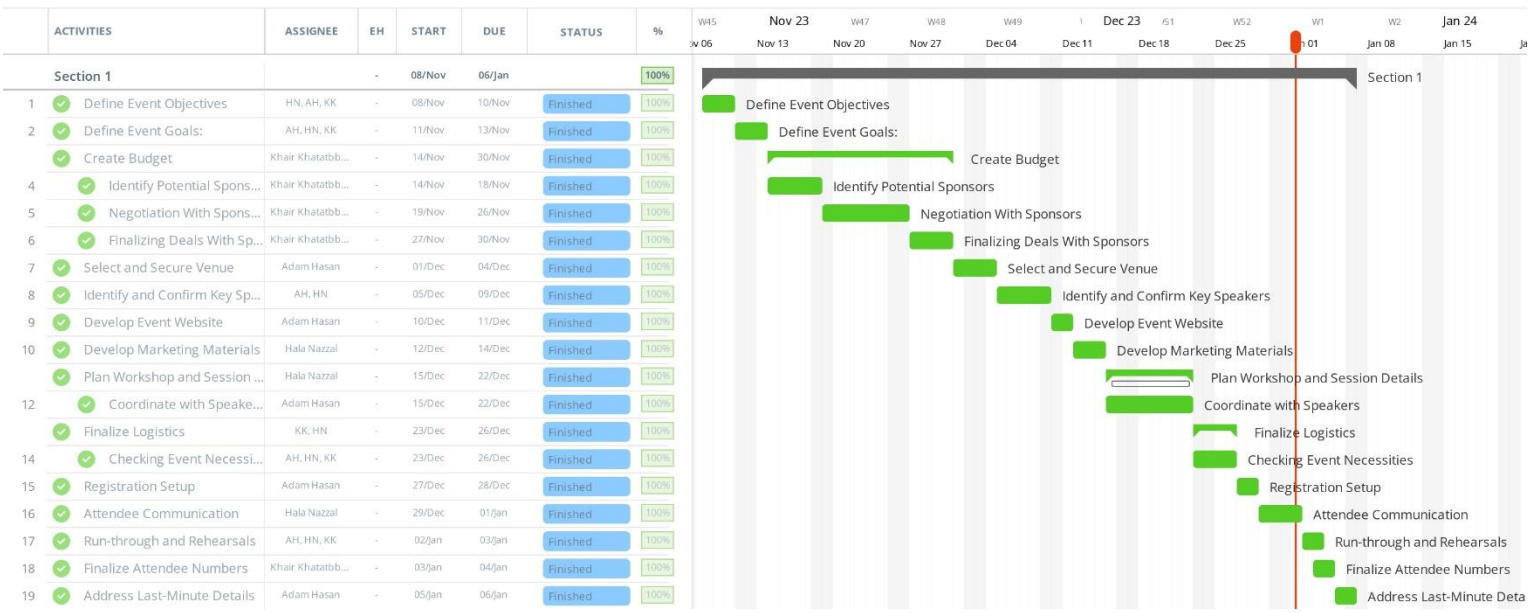

	ACTIVITIES	ASSIGNEE	EH	START	DUE	STATUS	%
	Section 1		-	08/Nov	06/Jan		100%
1	Define Event Objectives	HN, AH, KK	-	08/Nov	10/Nov	Finished	100%
2	Define Event Goals:	AH, HN, KK	-	11/Nov	13/Nov	Finished	100%
	Create Budget	Khair Khatatbb...	-	14/Nov	30/Nov	Finished	100%
4	Identify Potential Spons...	Khair Khatatbb...	-	14/Nov	18/Nov	Finished	100%
5	Negotiation With Spons...	Khair Khatatbb...	-	19/Nov	26/Nov	Finished	100%
6	Finalizing Deals With Sp...	Khair Khatatbb...	-	27/Nov	30/Nov	Finished	100%
7	Select and Secure Venue	Adam Hasan	-	01/Dec	04/Dec	Finished	100%
8	Identify and Confirm Key Sp...	AH, HN	-	05/Dec	09/Dec	Finished	100%
9	Develop Event Website	Adam Hasan	-	10/Dec	11/Dec	Finished	100%
10	Develop Marketing Materials	Hala Nazzal	-	12/Dec	14/Dec	Finished	100%
	Plan Workshop and Session ...	Hala Nazzal	-	15/Dec	22/Dec	Finished	100%
12	Coordinate with Speake...	Adam Hasan	-	15/Dec	22/Dec	Finished	100%
	Finalize Logistics	KK, HN	-	23/Dec	26/Dec	Finished	100%
14	Checking Event Necessi...	AH, HN, KK	-	23/Dec	26/Dec	Finished	100%
15	Registration Setup	Adam Hasan	-	27/Dec	28/Dec	Finished	100%
16	Attendee Communication	Hala Nazzal	-	29/Dec	01/Jan	Finished	100%
17	Run-through and Rehearsals	AH, HN, KK	-	02/Jan	03/Jan	Finished	100%
18	Finalize Attendee Numbers	Khair Khatatbb...	-	03/Jan	04/Jan	Finished	100%
19	Address Last-Minute Details	Adam Hasan	-	05/Jan	06/Jan	Finished	100%

Lina.Hammad Chat Files +

12/25/23 1:26 PM

تمام شكرا وانا كتير اسفه على الازعاج

12/25/23 1:37 PM

بس كمان لازم اعرف كم مفروض تاخدي على topic for one workshop

مشان احطهم بل cost

December 28, 2023

Lina.Hammad 12/28/23 7:51 PM

01:10

1

01:56

04:38

Sunday

Lina.Hammad Sunday 8:02 PM

https://www.linkedin.com/in/lina-hammad-1068a8106/

HTU professor -Orwa Aladaileh

Profile:

Android Developer at Adaptive TechSoft .

Experience

- Building applications for students and instructors for universities in KSA, Jordan
- Developed applications for monitoring and assistance in the brain field.

دكتور لازم عبي عنك مثل هيك معلومات عندك لينكد ان اشوف

Edited

وكمان بدي اعرف مثلا كم احط انك بتاخد بساعتين وركشوب لازم احط سعر

12/28/23 4:25 PM

ممكن بليز تساعدني

December 29, 2023

Orwa Aladaileh 12/29/23 5:37 PM


www.linkedin.com/in/orwah-aladayleh-5b84564a

هاد البروفايل تبعي

حطي مثلا 200 دينار على ال work shop

12/29/23 7:27 PM

تمام يسلم ايدك شكرا

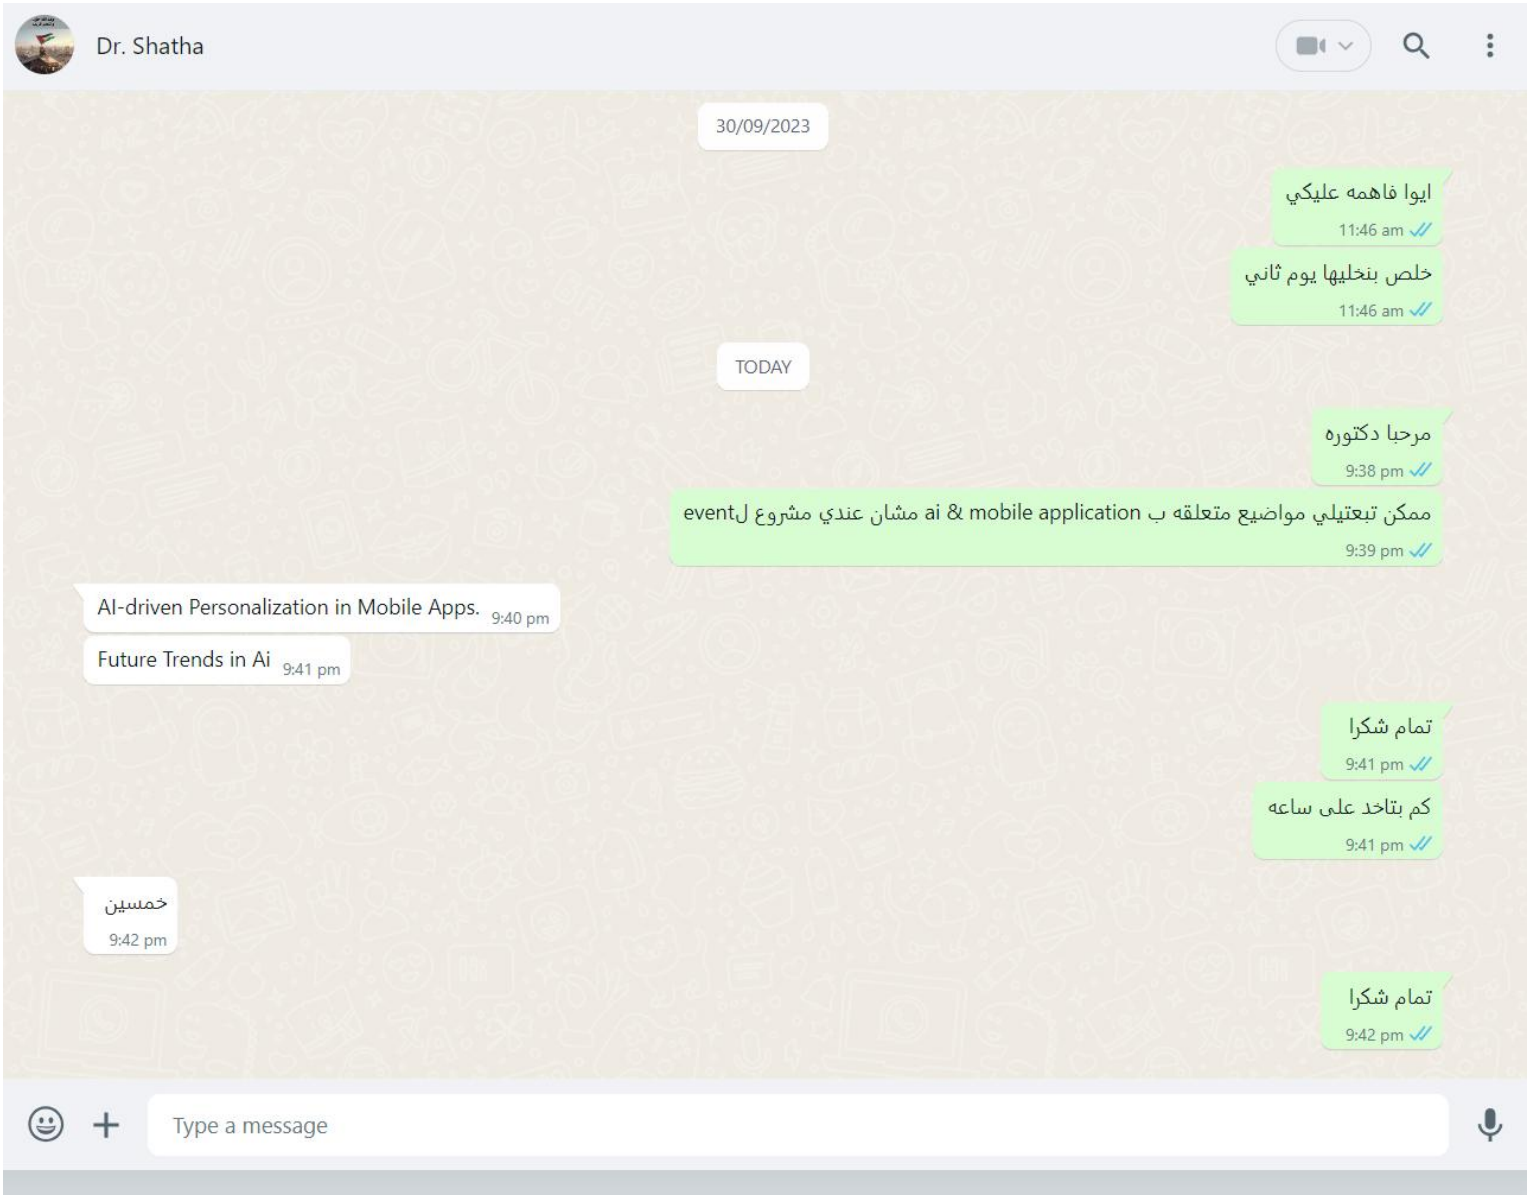
Dr. Shatha
30/09/2023
ايوا فاهمه عليكي
11:46 am
خلص بنخليها يوم ثاني
11:46 am
TODAY
مرحبا دكتوره
9:38 pm
ممكن تبعتيلي مواضيع متعلقه ب ai & mobile application مشان عندي مشروع لevent
9:39 pm
AI-driven Personalization in Mobile Apps. 9:40 pm
Future Trends in Ai 9:41 pm
تمام شكرا
9:41 pm
كم بتاخد على ساعه
9:41 pm
خمسين
9:42 pm
تمام شكرا
9:42 pm
Type a message

Dear QahwaBlk,

I trust this email finds you well. My name is Hala, and I am reaching out on behalf of Elite solution events. We are excited to confirm our upcoming event on 6th of January.

Our event is expected to host approximately 150 attendees, we would like to kindly request your support in providing complimentary coffee drinks for our attendees.

We understand the value of collaboration and are confident that your high-quality coffee products would be well-received by our audience, Our target audience are AI Experts and Researchers.,Developers and Programmers.,Technology,Investors ,Students and General Public.

If you have any specific requirements or preferences regarding your involvement in the event, please do not hesitate to let us know. We are more than willing to work together to ensure that your brand is effectively highlighted during the event.

Thank you for considering our request, and we look forward to the possibility of partnering with Qahwablk to make our event a resounding success. If you have any questions or require additional information, please feel free to email me.

Best Regards ,

Hala (Leader of Spark Elite)

One attachment • Scanned by Gmail ⓘ



from: **Hala** <halanazzal2020@gmail.com>
to: M@qahwablk.com
date: Jan 6, 2024, 10:44 PM
subject: Sponsorship Confirmation
nailed-by: gmail.com

Problems Encountered

We encountered a problem after the first day of the event after we checked everything, we got a call from our guest speaker that he couldn't give out the session because he has a family emergency of the 2 days

Problem Solving Application

PDCA

Is the first problem solving techniques that we used

PLAN:

The guest speaker didn't attend on the last day of the event sue to family emergency occurred, So there was no technical session and one hour was left empty in the schedule this was bad cause it will prevent us to establish our events goals which were keeping the attendees engaged to maintain the events overall quality also researching for a backup guest speaker to prevent the attendees to feel unsatisfied about the events also search for an alternative guest speaker to replace the old one within this short period of time.
So, we decided to develop a plan that outlines the measurement and to achieve our goals above based on certain timeline to go through which was 8 hours that we had
Which was first thing was dividing the members based on their swot analysis

DO:

Before dividing the tasks we decided to do brainstorming searching for solutions then we divided the tasks the first task was changing the schedule plan to a new one with the guest speaker and we Estimated the attendees point of view for not having a technical session and their expectation for it taking into consideration the stakeholder point of view and let them know what are we planning to do also asking them for their recommendation we then communicated with the attendees about what happened by sending emails and on the day of the session we decided to send the manger on the stage explaining what happened with the old speaker keeping the attendees updated we needed to finish all these by 4 hours
Then another team had 4 hours were searching into the old data event contacting the old speakers form the past events if there is any of them available pay them bonus if they can attend making sure that the replacement of the new guest speaker may result the same of the old guest speaker until we finally found one.

CHECK:

Checking if we met the goals this happened during the session and after helping us to evaluate the result:

1. We need to check the engagement level so, during the event we are going to observes if the audience are engaging with the guest speaker if no then we have to come up with new ideas to make the audience more engaged such as telling the speaker ask the audience about their perspective about the topic letting them to engage more with the topic sharing their ideas having different view of the topic this made us to insure QA (Quality assurance) of the event.
2. During the events we took the feedback of the audience directly and after the events we sent them a survey to take their feedback and what did they learned also ask them if it did benefit them.

ACT:

which is let us to know if what we did need improvement


1. Now after we collected the feedbacks, we are going to evaluate them to identify and analysis which part go the positive feedback to keep them in consider for the future events and which one didn't receive good feedback then highlight them for improvement identifying the issues to develop a new enhanced contingency plan to use in the future events.
2. Identifying any skills that were needed but we didn't have it
3. Create a documentation about the feedback and the improvement and the guest speakers that we went through to use it for future events
4. See the team idea what to improve and what needed to work on asking taking their opinion into consideration for the future events.

SWOT analysis: (Garfinkle, 2023)

Strengths (Current)	**Weaknesses (Current)**
1. Having such as this problem and solve it in a short time will increase the teamwork and make the member to be more quick-witted to the future problem that might occurs making them more adapted to bigger problems. 2. replacing the old guest speaker with a new speaker with different experience and knowledge this will give the attendees more than one experience and knowledge to learn from this stuff will make them to benefit more from the event. 3.keeping the session and having different style to explain will make the engagement continues between the speaker and audience this will maintain the overall event quantity. 4. Gaining the trust of the audience being able to find and replace the speaker with the old one within a short period of time.	1.That the new guest speaker may have different way to approach the audience or not good body language as the old guest speaker 2. Having only half day to find a suitable speaker might panic the team member. 3.Lacking of familiarity for the speaker might cause him to not to match perfectly with the goals that we had which might affect him to deliver those important ideas to the audience 4.the audience might not trust the new speaker experience and knowledge as the old one. 5.giving the speaker a short time to prepare it will be challenge for him a there is a risk that he might not have time to prepare properly.

Opportunities (Future)	Threats (Future)
1. Sharing new knowledge and experience that will be transferred to the audience is a good opportunity. 2. The audience might gain have another chance to engage with the speaker and they might like the new speaker way more causing the session to be more interactive. 3. Showing the audience that we solved this problem this will make us to gain the trust of the attendees to attend more event that our company hold. 4. The new speaker might have more practical experience of the world this will help the audience to have insight of the AI mobile application new trend and insight of the future of the topic.	1. The attendees might be not satisfied with the new speaker because he didn't meet their expectations. 2. The urgency of finding a guest speaker quickly and within a short period of team might lead to choose not the most suitable guest speaker. 3. If the attendees got disappointment form the guest speaker, they might share this on the social media which will affect our company image and the events image.

Root Cause Analysis (RCA): (Birt2022 ،)

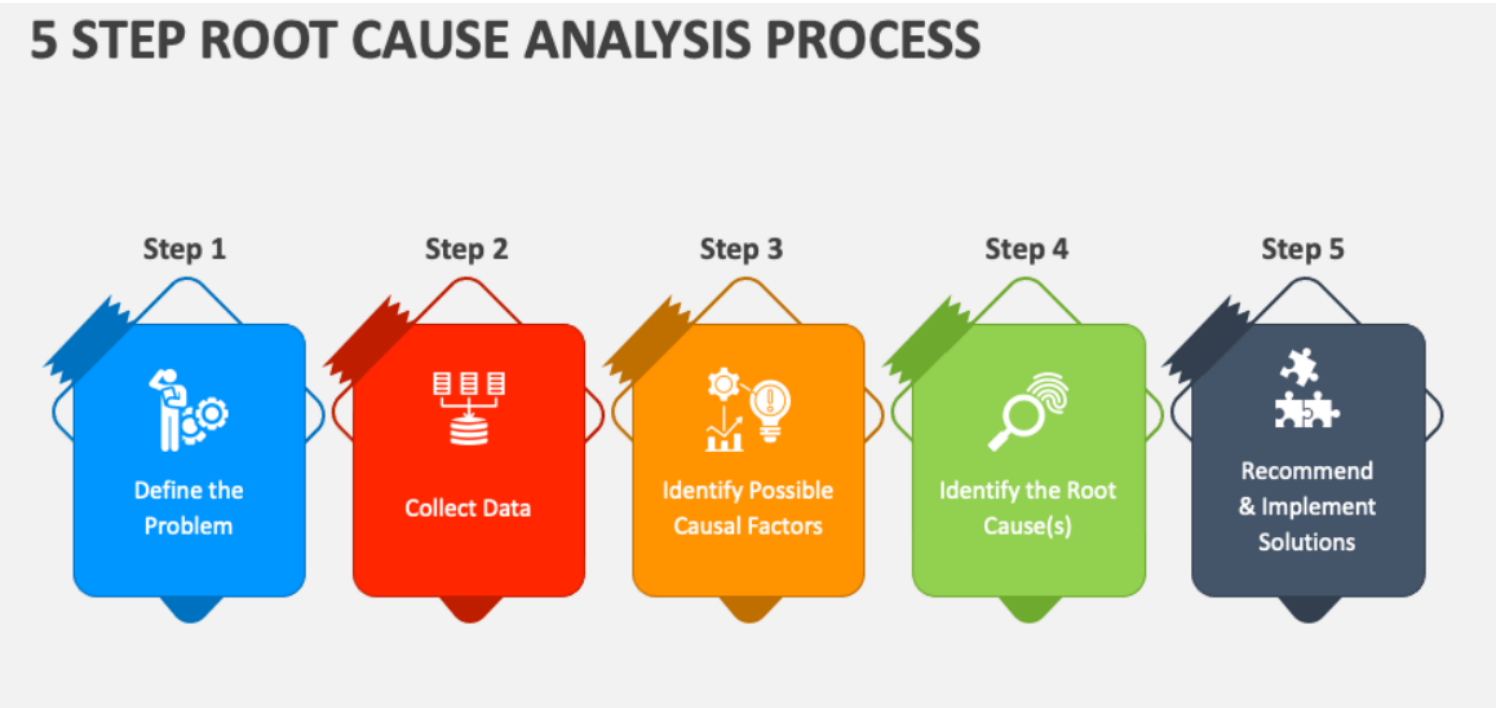

Part 1 Define the problem:

The absence of the guest speaker on the last day of the event due to family emergency leading to have 1 hour gap technical session left to fill in.

Part 2 collect the data:

First data was to communicating is from the guest speaker himself checking what was has emergency understand it if it can be solve but unfortunately, we couldn't. Therefore, we discussed the problem with the stakeholder taking their ideas and advices into consideration on what to do next then we estimated the attendees point of not having the old guest speaker.

Part 3 possible cause factors:

1.Lack of Contingency Plan that we had:

Lacking of having a backup speaker data to look into which will save us time.

2.Limited time for the replacement we had:

Having only 8 hours left to find a good replacement with similar background as the old one was a quiet challenge that we had to solve.

3.Lack of communication with the guest speaker:

Not checking on the guest speaker daily lead us to know the problem late

Part 4 Identify the root cause:

1.Failing to monitor the speaker availability: leading us to know the problem late causing a delayed solution.

2.Having only one channel to communicate with the guest speaker: such as only sending email this will lead the team to have an unreliable delivery of the emergency cause the guest speaker might be experiencing an internet issue so he couldn't inform them and there was no another channel such as phone calls to communicate through

Part 5 recommendation and Implementation Solutions:

1.Enhancement of Contingency Plan:

Putting a new plan that include a list of a backup speakers that we can replace with if anything occurs.

2.Put some protocols and new agreements with the speaker:

Putting some protocols telling them about the importance if any emergencies happen, they should notify us first and some agreement so that if they came up with anything they should give us a contact of a new speaker to replace them in the event this will help us to solve the problem more quickly and efficient**.**

3.Hold a training:

Regular training will help the team member think in the right way to take the right & quick decision.

After we did the RCA, we made a decision based on variety voting that was made between the members in the team and the data that we had in RCA that we decided to bring a new guest speaker to replace the old one.

Methodology

It is our belief that having the right methodology is crucial for the success of any project as it can bring Consistency, Improved Planning, Effective Communication to managing projects. In project management methodologies like Agile, Scrum, or Waterfall provide frameworks for planning and executing projects. Our decision is to adopt the Scrum methodology as it best suits us.

Scrum serves as a project management framework. Its main objective focuses on enhancing communication, collaboration and efficiency, within teams.

The product owner, Scrum Master, and the Development Team Members are the majorly Scrum development roles.


Our justification for choosing this specific methodology is its Flexibility and Adaptability, Continuous Improvement and Risk Management.

Flexibility and Adaptability: In an environment where priorities can switch quickly, Scrum provides a framework that allows for regular review and adjustment.

Continuous Improvement: At the end of each sprint the team holds a review and reflects on it, Learning from both our successes and failures. Using that gained knowledge to improve our project.

Risk Management: With daily team collaborations via meetings, we can identify and address risks early in the development process.

Utilization of the Scrum methodology was executed as follows.

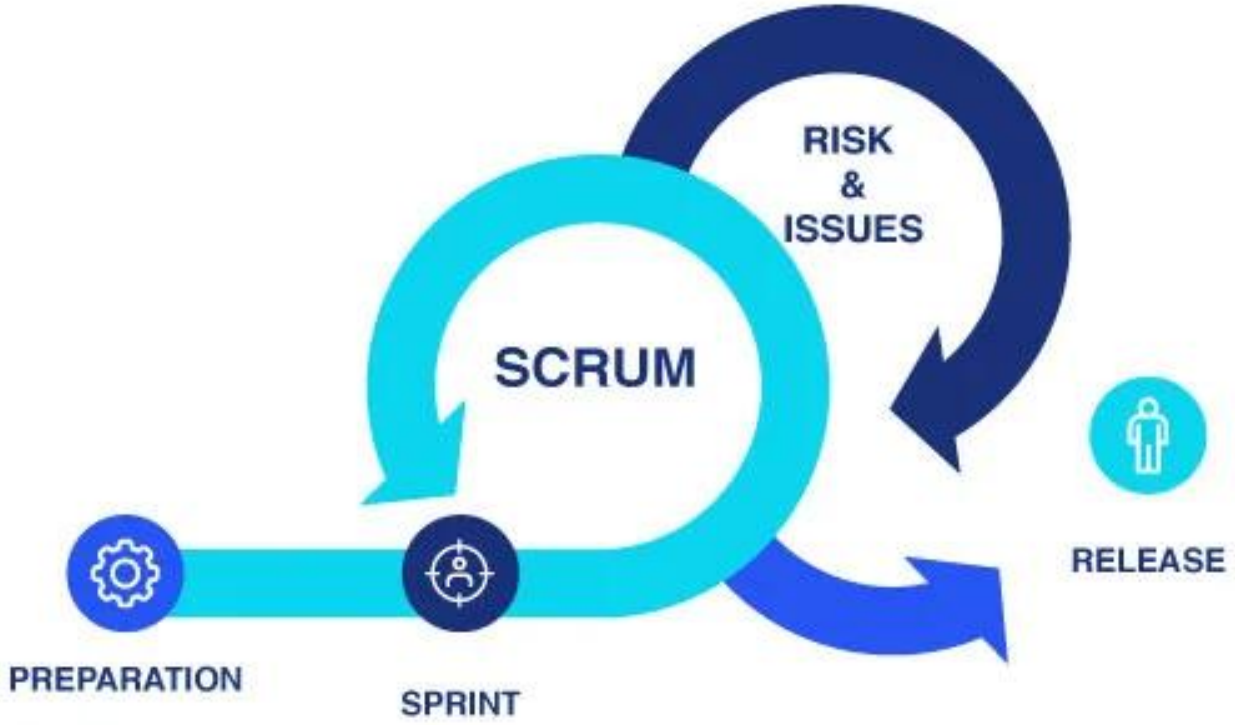

Initiation: The initiation phase starts by assigning the Scrum master, Creating a vision for the project.

Preparation: The Scrum Master presents the project requirements for the team with creating a sprint backlog for tasks which must be completed such as venue selection, marketing and promotion, sponsorships, speaker coordination, logistics.

Implementation: Team members start executing their sprints and removing tasks as team members complete them and assigning out new tasks from the backlog as needed, meeting to provide project updates and review the work plans or concerns.

Review: Scheduling meetings with the team members and stakeholders to give them feedback and updates while also to discuss what went well and where there are areas for improvement based on the results of the completed sprint.

Releasing: We deliver any final updates to our stakeholders and organize a project retrospective meeting with our team to analyze the performance of each individual sprint and to discuss the overall performance of the project.

Event Evaluation

1. Profitability:

We succeeded in attracting sponsors who contributed greatly to covering the expenses paid

Appropriate scheduling of ticket prices, which was also one of our profit bases

2. Resource Utilization:

- Exploiting sponsors by attracting a large number of attendees by publishing advertisements on social media

- Scheduling events in an appropriate manner so that we make full use of the time

- According to the prior media success of the event, some companies were keen to place advertisements for themselves through posters, brochures, etc.

- Exploiting the hotel's human staff in hospitality, reception and service, and thus we reduced the number of our employees

3. Time Allocation:

Scheduling time in a logical and appropriate way, where priorities were determined and the time of each event was divided based on how much time it needed

- Informing all crew of the schedule and giving them the right to improvise decisions within a specific methodology

- Because there are activities that depend on a person (like, just speaker),

We have made an agreement with alternative people.

References

Bibliography

Birt, J., 2022. *Decision-Making and Problem-Solving: What's the Difference?.* [Online]
Available at: https://www.indeed.com/career-advice/career-development/problem-solving-and-decision-making
[Accessed 4 1 2024].

Garfinkle, J., 2023. *MOTIVATIONAL SPEAKERS: HOW TO TELL THE GOOD FROM THE BAD.* [Online]
Available at: https://joelinspirationalspeaker.com/articles/pros-cons-motivational-speakers/
[Accessed 2 1 2024].

Gravelle, C., n.d. *The Importance of Time Management in Event Planning.* [Online]
Available at: https://eventeem.co.uk/the-importance-of-time-management-in-event-planning/
[Accessed 25 12 2023].

Grip, 2022. *7 tips for time management skills in events.* [Online]
Available at: https://www.linkedin.com/pulse/7-tips-time-management-skills-events-gripevents/
[Accessed 25 12 2023].
